Lab 5

1. Reports

a. Cost overview

COST OVERVIEW

MON 10/31/22   FRI 1/20/23

COST
67,106,250 đ

REMAINING COST
30,346,875 đ

% COMPLETE
51%

COST STATUS
Cost status for top level tasks.

| Name	Actual Cost	Remaining Cost	Baseline Cost	Cost	Cost Variance
IoT system	36,759,375 đ	30,346,875 đ	65,606,250 đ	67,106,250 đ	1,500,000 đ

PROGRESS VERSUS COST
Progress made versus the cost spent over time. If % Complete line below the cumulative cost line,your project may be over budget.

COST STATUS
Cost status for all top-level tasks. Is your baseline zero?
Try setting as baseline

b. Resource overview

RESOURCE OVERVIEW

RESOURCE STATS
Work status for all work resources.

WORK STATUS
% work done by all the work resources.

RESOURCE STATUS
Remaing work for all work resources.

Name	Start	Finish	Remaining Work
Dinh Huy Thien - MNG/TEST	Mon 10/31/22	Thu 12/8/22	145.5 hrs
Nguyen Minh Anh - DB/BE	Tue 11/1/22	Wed 12/7/22	8 hrs
Huynh Gia An Tien - NET	Thu 11/3/22	Wed 12/7/22	44 hrs
Nguyen Trung Nguyen - BA	Mon 10/31/22	Thu 12/15/22	24 hrs
Nguyen Khuong - FE	Thu 11/3/22	Wed 12/7/22	110.5 hrs
Lam Minh Quan - UI	Thu 11/3/22	Wed 12/7/22	24 hrs
Nguyen Tien Duong - ELEC	Tue 11/1/22	Wed 12/14/22	49 hrs

c. Work overview
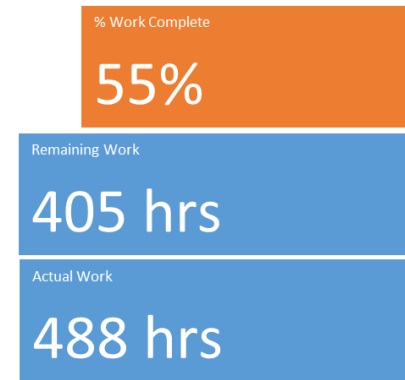
WORK STATS
Shows work stats for all top level tasks.

% Work Complete

55%

Remaining Work

405 hrs

Actual Work

488 hrs

WORK OVERVIEW

Mon 10/31/22 — Fri 1/20/23

RESOURCE STATS
Shows work stats for all your resources.

REMAINING AVAILABILITY
Shows remaining availability for all work resources.

2. **Print & Save as PDF file**
3. **Reports**
   a. Báo cáo tiến độ dự án

BURNDOWN

WORK BURNDOWN

Shows how much work you have completed and how much you have left. If the remaining cumulative work line is steeper, then the project may be late. Is your baseline zero?

Try setting a baseline

TASK BURNDOWN

Shows how many tasks you have completed and how many you have left. If the remaining tasks line is steeper, then your project may be late.

Learn more

b. Báo cáo họp nhóm

Báo cáo họp nhóm

Name	Start	Finish	% Complete	Actual Cost
Analysis and design	Mon 10/31/22	Mon 10/31/22	100%	1,350,000 đ
Documents	Tue 11/1/22	Thu 11/3/22	100%	2,875,000 đ
First meeting	Thu 11/3/22	Thu 11/3/22	100%	356,250 đ
Database setup	Fri 11/4/22	Wed 11/9/22	100%	1,500,000 đ
Backend	Thu 11/10/22	Thu 12/8/22	66%	8,700,000 đ
UI / UX designing	Fri 11/4/22	Mon 11/14/22	57%	2,000,000 đ
Front-end	Tue 11/15/22	Wed 12/7/22	38%	4,093,750 đ
Circuits	Fri 11/4/22	Mon 11/28/22	76%	5,150,000 đ
Others	Fri 11/4/22	Thu 12/8/22	39%	10,734,375 đ
Annouce to users	Fri 12/9/22	Mon 12/12/22	0%	0 đ
Execute the Training Plan	Tue 12/13/22	Tue 12/13/22	0%	0 đ
Install the system	Wed 12/14/22	Wed 12/14/22	0%	0 đ
Post-Deploymen	Thu 12/15/22	Thu 12/15/22	0%	0 đ

c. Báo cáo tổng kết dự án

PROJECT OVERVIEW

MON 10/31/22   FRI 1/20/23

% COMPLETE

51%

MILESTONES DUE
Milestones that are coming soon.

Name	Finish

% COMPLETE
Status for all top-level tasks. To see the status for subtasks, click on the chart and update the outline level in the Field List.

LATE TASKS
Tasks that are past due.

Name	Start	Finish	Duration	% Complete	Resource Names
Login	Mon 11/14/22	Wed 11/16/22	3 days	67%	Nguyen Minh Anh - DB/BE
Wireframe	Tue 11/8/22	Mon 11/14/22	4 days?	25%	Lam Minh Quan - UI
